



Arlington High School Building Project

AHS Construction Update – July 6, 2023

Arlington HS Construction Schedule: April 2020 – September 2025

Construction Details


Phase 1 construction is complete and the new Performing Arts and Science, Technology, Engineering, Arts & Mathematics wings are open. Phase 2 began immediately after the Phase 1 building turnover. Part of the old school has been demolished and that area is closed off from the existing school during the next phase of construction.

COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.



PHASE 2 BUILDING CONSTRUCTION (February 2022 – October 2023)

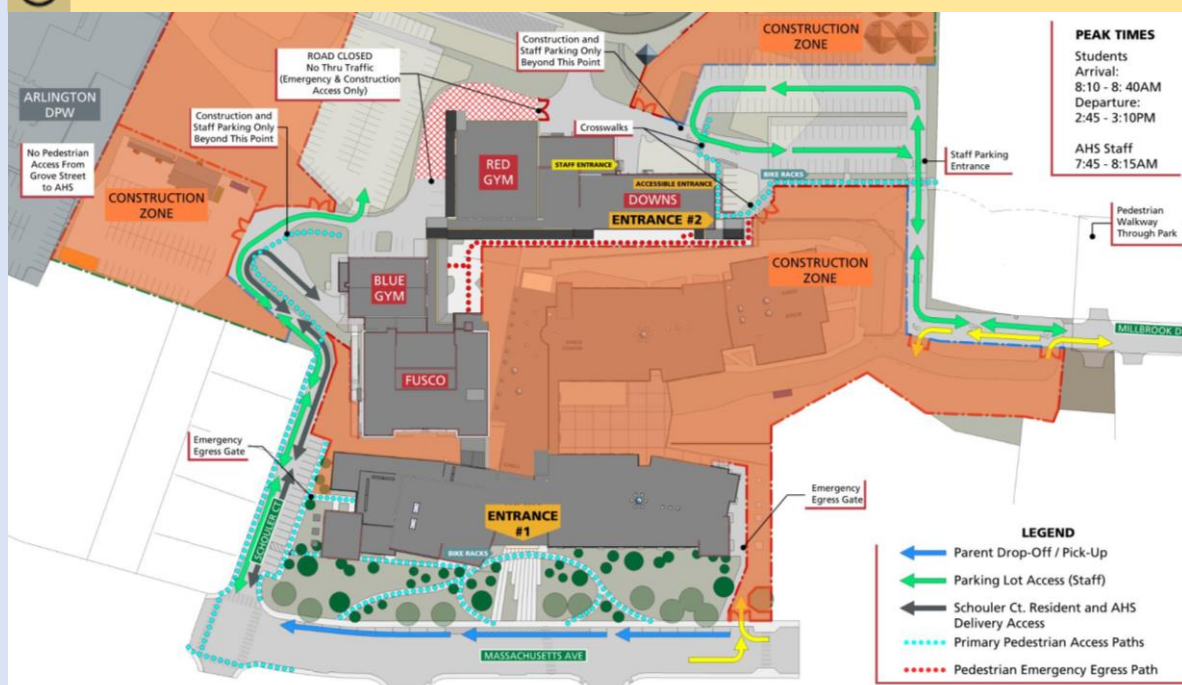

Construction Look Ahead – Week of July 10th, 2023

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts:

- Deliveries ongoing
- Paving on Mill Brook Drive. Entrance to Brigham Square Apt. and 22 Mill Street will be impacted. Police detailing will be provided to direct traffic.
- From 6/24/23 through 8/25/23 access to school parking and fields via Mill Brook Dr. will be closed. The only access to Peirce Field and school parking will be from Schouler Ct. (via Mass Ave.) See Photo 1 for details.

General Site Activities:

- Phase 2:
 - Installation of windows, curtain walls, and masonry
 - Installation of drywall, ceramic tiles, ceiling grids, and flooring
 - Installation of door frames, interior windows, and casework
 - Install mechanical, electrical, plumbing, and fire sprinklers
 - Painting
 - Grading and paving of Mill Brook Drive
 - Dust mitigation ongoing
- Material Stockpile/Temp Construction Lot for contractor storage and parking
- Schouler Court:
 - Construction vehicles entering and exiting project site

Weekend Work/Holiday Work/Night Work:

- Saturday work is required for the foreseeable future

Sign up for Weekly Construction Updates
<https://ahsbuilding.org/news/construction-updates/>
 For more information, visit:
www.ahsbuilding.org
 Email questions or concerns to:
ahsbuilding@arlington.k12.ma.us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative,
 (617) 352-8593



Skanska USA Inc.
Owner's Project Manager



Consigli Construction Co., Inc.
Construction Manager at Risk



HMFH Architects, Inc
Architect

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF JULY 10TH, 2023

Photo 1:

Site Logistic Plan for 6/24/23 – 8/25/23.

All vehicle access to Peirce Field and school parking will be from Schouler Ct. (via Mass Ave.)

Arlington High School



Summer 2023 Logistic Plan
06/24/23 - 08/25/23

Temporary Staff and
Bus Parking
06/24/23 - 08/25/23

CONSTRUCTION
OFFICES, LAYDOWN
AND PARKING

All Traffic use
Schouler Ct.
06/24/23 - 08/25/23

Millbrook Drive CLOSED
to Traffic
06/24/23 - 08/25/23

8/25/23

MILLBROOK DR

PEIRCE FIELD

MATERIAL STOCKPILE
ZONE

ARLINGTON
DPW

Temporary Staff and
Bus Parking
06/24/23 - 08/25/23

CONSTRUCTION
OFFICES, LAYDOWN
AND PARKING

All Traffic use
Schouler Ct.
06/24/23 - 08/25/23

Millbrook Drive CLOSED
to Traffic
06/24/23 - 08/25/23

8/25/23

MILLBROOK DR

PEIRCE FIELD

MATERIAL STOCKPILE
ZONE

ARLINGTON
DPW

- LEGEND**
- PRIMARY CONSTRUCTION ACCESS
 - SECONDARY CONSTRUCTION ACCESS
 - SCHOOL DROP-OFF AND PICK-UP
 - PARKING LOT ACCESS
 - SCHOULER CT AND AHS DELIVERY ACCESS
 - PRIMARY PEDESTRIAN SCHOOL ACCESS
 - WORKER ACCESS TO AUDITORIUM
 - CONSTRUCTION GATE
 - DRIVEN CONSTRUCTION FENCING
 - PANELIZED CONSTRUCTION FENCING
 - EXISTING FENCING

Finish grade binder
course asphalt

PHASE 2 CONSTRUCTION

MASSACHUSETTS AVE

MASSACHUSETTS AVE

PERFORMING ARTS

FLUSCO

TEMPORARY CONNECTOR

MAIN ENTRANCE #1

STEAM

DOWN

RED GYM

BLUE GYM

SCHOULER CT

10

39

55

18

13

15

16

17

19

20

21

22

23

24

25

26

27

28

29

30

31

32

33

34

35

36

37

38

40

41

42

43

44

45

46

47

48

49

50

51

52

53

54

56

57

58

59

60

61

62

63

64

65

66

67

68

69

70

71

72

73

74

75

76

77

78

79

80

81

82

83

84

85

86

87

88

89

90

91

92

93

94

95

96

97

98

99

100

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF JULY 10TH, 2023



Photograph 2: Phase 2 East Elevation (Mill Brook Dr)



Photograph 3: North Main Entrance

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF JULY 10TH, 2023



Photograph 4: Installation of flooring and ceiling grid in a classroom



Photograph 5: Radiant floor piping at north main entrance lobby
